

A PROPOSAL FOR

MARSAL

مرسال

Brand evolution, a consolidated bilingual identity,
and the collateral that carries it.

PREPARED BY

Miradore Experiences

DATE

6 August 2026

DELIVERY

24 August 2026

INVESTMENT

SAR 24,000

RIYADH
6 AUG 2026

To the team at Marsal,

Thank you for the call last week, and for sending across the logo files. We have spent a few days with them, put them through the places they actually have to live, and this proposal is what came out of that.

The short version: you do not need a new logo. The one you have is doing its job, and there is real equity in it already sitting on your paperwork, your vehicles and your invoices. Redrawing it would be an expensive way to solve a problem you do not have.

What you do need is for that logo to work harder in the places it currently struggles. It has no short form, so there is nothing clean to put in a profile picture or an app icon. And when the Arabic and the English sit together, the signature runs wide and low - which is why it keeps getting shrunk into illegibility on cards, on nav bars, and on the side of a truck.

So the work here is evolution, not replacement. We pull a proper logomark out of the identity you already own. We consolidate the bilingual signature so Arabic and Latin hold equal weight in a footprint that fits. Then we build out the everyday pieces - cards, letterhead, profile pictures, social templates, the website - so the next hundred things Marsal produces look like they came from the same company.

One thing worth saying plainly, because it shapes both the price and the schedule: we are not going to hand you a spread of logo options to pick from. We will do the thinking, commit to one direction, and show it to you applied to real things - a card, a truck panel, a profile picture - so you are judging a decision rather than a shape on a white page. If it is wrong, we adjust it.

Work starts Monday 10 August and everything lands with you on Monday 24 August, with two review points along the way so there are no surprises at the end.

If any part of this reads as more, or less, than what you had in mind, tell us and we will reshape it. We would much rather adjust the scope now than hand you something you have to explain internally.

Warm regards,

Adeel Ahmed

Director / Miradore Experiences

CONTENTS

01	Where the identity stands today	03
02	What we are proposing	04
03	Scope of work, phase by phase	05
04	Delivery schedule	07
05	Investment and terms	08
06	What we need from Marsal	09

01

Where the identity stands today

An honest read of the current logo, and the three things holding it back.

This is not a criticism of the mark. It is a list of the jobs it is being asked to do that it was never drawn to do. All three are fixable without losing anything you have already built.

01

There is no short form

Every strong logistics brand carries two assets: a full signature for documents and letterhead, and a compact mark for everything else. Marsal has only the first. A profile picture becomes a squeezed wordmark, an app icon is not possible, and there is nothing to stitch onto a uniform, cut into vinyl for a vehicle door, or stamp onto a seal. Below roughly 25 mm wide, it simply stops reading.

02

The bilingual lockup runs too wide

Placed side by side, the Arabic and English signature becomes long and shallow. In a business card corner, a website navigation bar or a truck panel, the only way to fit it is to scale it down until neither language is legible. The two scripts also carry different optical weights, so one visually dominates the other depending on the size.

03

Collateral is being made one piece at a time

Without an agreed system for colour, type and spacing, every new card, post or document is a fresh set of decisions. It is slower, it costs more over a year, and the drift shows - especially to the enterprise clients and government tenders where visual consistency is read as operational discipline.

02

What we are proposing


Three moves. Everything else in this document follows from them.

A
THE MARK

A logomark drawn out of the logo you already own


We do not start with a blank page. We take the existing Marsal logo apart, find the element carrying the most recognition, and develop it into a mark that stands alone. It has to survive four tests before we present it: legible at 16 pixels, readable in a single colour, cuttable in vinyl without detail loss, and distinct from the other logistics marks operating in the Kingdom.

One direction, developed properly - not a spread of options to choose between. We show it applied to real things, so you are judging a decision rather than a shape on a white page.

B
THE SIGNATURE

One consolidated bilingual signature, in three footprints

Arabic and Latin are matched on a shared baseline, with optical weights and heights tuned so neither script overpowers the other. One signature that holds together at any size, delivered in three configurations - each with a defined minimum size and clear-space rule, so nobody has to guess which version to use.



Indicative construction. The mark itself is Phase 02 work - the placeholder above stands in for it.

C
THE SYSTEM

A system light enough that your team will actually use it

Colour, typography, a supporting graphic device and clear placement rules - documented in a guidelines file people can read in fifteen minutes, not a 120-page manual that gets opened once. Everything ships with editable working files, so your team can produce day-to-day material without coming back to us for every post.

03

Scope of work, phase by phase

Seven phases, all delivered inside the same window.

Phase 01 Read and audit

10 - 11 AUG

- Review of the existing logo files, current collateral, and how the mark is being applied today
- Benchmark of eight to ten logistics identities operating in KSA and the wider Gulf
- A working session with your team - what the brand needs to carry, and where it keeps failing
- A one-page direction note, agreed before any design begins

Phase 02 Logomark and bilingual signature

11 - 17 AUG

- The logomark, developed from the existing Marsal logo and presented in application
- Full construction: proportion grid, clear space, minimum sizes
- Consolidated bilingual lockups - horizontal, stacked and mark-only
- One-colour, reversed, mono and vinyl-cut versions for production
- Icon renderings at 16, 32, 64, 128 and 512 px, plus favicon and app-icon files
- Master artwork delivered as AI, EPS, SVG, PDF and PNG

Phase 03 Core brand system

17 - 18 AUG

- Colour palette with print (CMYK, Pantone), screen (RGB, HEX) and fleet references (vinyl and paint codes)
- Typography: a matched Arabic and Latin pairing with weights, hierarchy and usage rules
- One supporting graphic device drawn from the mark, for backgrounds, edges and pattern
- Iconography direction and photography art direction for fleet, facility and team imagery

Phase 04 Print and corporate collateral

18 - 20 AUG

- Business card, bilingual, both faces, print-ready with bleed and crop marks
- Letterhead and continuation sheet - print version plus an editable Word template for daily use
- Envelopes, DL and A4, and a document folder
- HTML email signature, bilingual, tested in Outlook and Gmail
- Operational document set: quotation, invoice, delivery note and waybill layouts
- Staff ID card, lanyard and uniform placement guide
- Fleet identity art direction - truck panel, van and container door placement

Phase 05 Digital and social

19 - 23 AUG

- Profile picture set, correctly cropped and sized for LinkedIn, Instagram, X, WhatsApp Business and Google Business
- Cover and banner artwork for each platform
- Nine social post masters - announcement, service, milestone, hiring, client quote, route and network, seasonal greeting, event, and a general-purpose layout
- Each master supplied in feed and story format, bilingual, as editable files
- A 16:9 presentation template, twelve master slides, for tenders and client meetings

Phase 06 Website design

19 - 23 AUG

- Sitemap and wireframes for five key pages: Home, Services, Fleet and Network, About, Contact and Quote Request
- Full visual design of the Home page and one inner page, desktop and mobile
- A UI component kit - buttons, cards, forms, navigation, footer - so the remaining pages can be built consistently
- Bilingual layout logic, including right-to-left behaviour for the Arabic version
- Developer-ready handoff in Figma, with specs and exported assets

Phase 07 Guidelines and handover

23 - 24 AUG

- Brand guidelines document covering the mark, lockups, colour, type, collateral and digital application
- Organised master file library, named and structured so files can be found without us
- A handover walkthrough with your team
- 14 days of post-handover support for file and format questions

REVISIONS

Two rounds of consolidated feedback are included at each review point. Further rounds, or a change of direction after the mark has been signed off, are quoted separately before any work begins.

What lands in your hands on 24 August

Counted out, so the scope above is easy to check against what actually arrives.

01

logomark, developed and production ready

03

lockup footprints, plus reversed and one-colour

07

print and corporate collateral items

05

profile picture sets, sized per platform

09

social post masters, in feed and story

12

presentation master slides, 16:9

05

website pages designed or specified, with UI kit

01

guidelines document and master file library


Every item is supplied in both an open, editable working file and a ready-to-use export, in the formats your printers and developers will ask for.

04

Delivery schedule

Kick-off Monday 10 August. Final handover Monday 24 August 2026.

Eleven working days across two weeks. Phases overlap deliberately - collateral, social and website design all begin from the same approved signature, so they progress in parallel rather than in a queue. Your input is only needed at the two review points marked in orange.

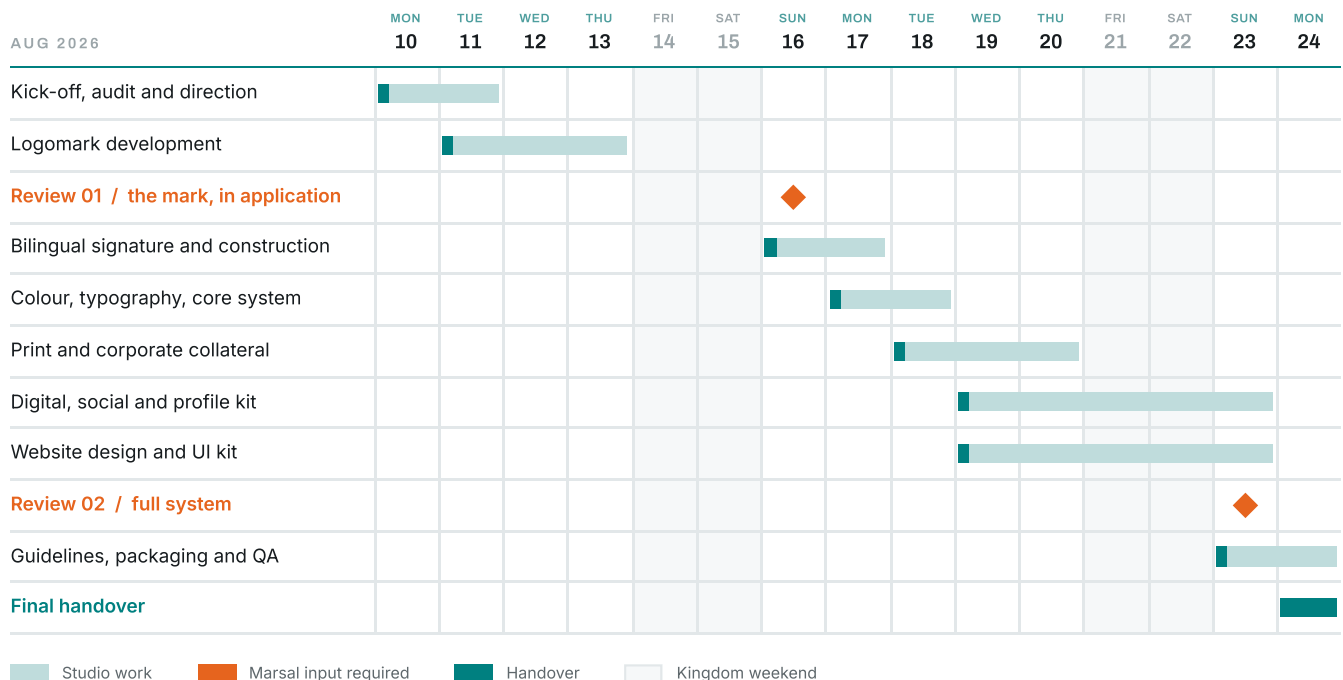

SUN 16 AUG

Review 01

The mark presented in application - on a card, a truck panel, a profile picture. You approve, or we adjust.

SUN 23 AUG

Review 02

The full system applied - card, letterhead, social, website - reviewed together.

MON 24 AUG

Handover

Every file delivered and organised, with a walkthrough for your team.

WEEKENDS

Two Kingdom weekends fall inside the window - 14 to 15 and 21 to 22 August. Our studio keeps a reduced working pass across them so the schedule holds, and no input is needed from your side on those dates.

DEPENDENCY

Phase 02 cannot start until the existing logo is supplied in vector format and a single approver is named. Everything downstream moves with that date.

05

Investment and terms

One fee, broken down so you can see where the effort sits.

PHASE		SAR
01	Read and audit	1,500
02	Logomark and bilingual signature	7,000
03	Core brand system	3,000
04	Print and corporate collateral	4,000
05	Digital and social	3,500
06	Website design	3,500
07	Guidelines and handover	1,500
TOTAL		SAR 24,000

INCLUDED IN THE FEE

- All design, artwork and file preparation across the seven phases
- Two rounds of consolidated revisions at each review point
- Full ownership of the final approved artwork, transferred to Marsal on settlement
- Editable working files and an organised master library
- 14 days of support after handover

NOT INCLUDED

- Printing and physical production of any item
- Website development and hosting - design only at this stage
- Photography and video production, should new imagery be required
- Third-party font licences, if a commercial typeface is selected
- Vehicle wrap production and fitting
- Trademark filing and registration

PAYMENT

50% on written confirmation to proceed, 50% on final handover. Bank transfer to Miradore Experiences, Riyadh.

VALIDITY

This proposal holds for 30 days from 6 August 2026. The 24 August delivery date assumes confirmation by Sunday 9 August.

IF IT FLEXES

Website design is the one block that can be deferred without weakening anything else - the mark, the bilingual signature and the collateral all stand on their own, and the fee reduces by SAR 3,500 if you would rather take it up later. Equally, if you want fleet livery production artwork or a full tender document set added, say so and we will price it against the same schedule.

06

What we need from Marsal

Five things. Nothing that should take more than an hour to gather.

- The existing logo in vector format - AI, EPS or SVG. A PNG or JPG will not carry us through print or vehicle production.
- One named approver. This schedule does not survive design by committee, and it is the single biggest risk to the date.
- Your Arabic legal name exactly as registered, plus CR number, VAT number and the address block for stationery.
- Contact details for cards and email signatures - names, titles in both languages, numbers.
- Two or three photographs of the current fleet and facility, so the art direction is built on what Marsal actually looks like.

HOW IT RUNS

You will hear from us at two points, not ten. The first is the mark, shown in application, where you approve a direction. The second is the full system review, where you see everything together - card, letterhead, social, website - before we finalise. Between those points we work, and we do not send fragments for reaction. It keeps the decisions clean, and it keeps the date.

CONFIRMATION TO PROCEED

Signing below confirms the scope, fee and schedule set out in this document, and authorises Miradore Experiences to begin work.

NAME AND SIGNATURE, FOR MARSAL

TITLE

DATE

Any questions before you sign, call us. We would much rather talk it through than have you agree to something on paper that does not match what you pictured.

MIRADORE EXPERIENCES

Riyadh, Kingdom of Saudi Arabia / hello@miradore.co / miradore.co
